

Construction Update

32nd Avenue
March 23, 2010



Crews will begin removing excess materials to free up work space.

Eight bathrooms on the south side have been tiled. Grout will be applied this week.

Nine headwalls have been cut and the one in the bariatric room has been set in place. Mounting will begin on March 24.

Can lights are mounted. Outlets are being installed where possible.

There are one set of cabinets and two countertops left to install. The crew will go back and level all the doors when installation is complete.

Legs were added to the nurse's station counter for more support.


Piping is complete in the mechanical room. There will be a few things to finish when the tie-in is done.

On Monday, March 29, crews will begin installing the flooring. Hallway carpeting will be done last.

In radiology, the machines will be set up and calibrated on Monday.

Sixth floor plumbing that is installed has been inspected. Ceiling grids will be done next week. The crew will be sheetrocking on Monday or Tuesday.

Construction area access is restricted. Please refrain from entering the 3rd floor clinic side.

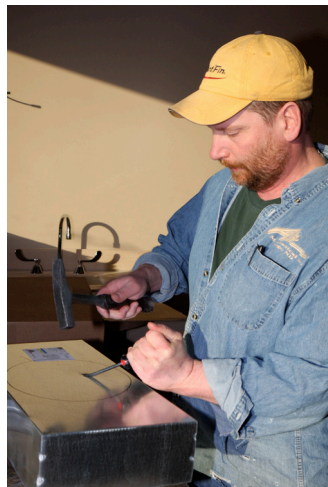

Innovis Health
